

Work Order ID 124378

124378

Page 1

Item ID: D4635-043 **Accept** ***N900040100*** **Setup Start *NS1***
Revision ID: **Stop *NS2***
Item Name: Aft Ceiling Panel Assembly, LH
Start Date: 9/10/14 **Start Qty:** 1.00 ***1*** **Cust Item ID:**
Required Date: 9/10/14 **Req'd Qty:** 1.00 ***1*** **Customer:**
Reference:

Approvals: **Process Plan:** MCS **Date:** 14-09-17 **Tooling:** _____ **Date:** _____ **Run Start *NR1***
QC: _____ **Date:** _____ **SPC (Y/N):** _____ **Date:** _____ **Stop *NR2***

| Sequence ID/ Work Center ID | Operation Description | Set Up/ Run Hours | Tool ID | Tool # | Plan Code | Accept Qty | Reject Qty | Reject Number | Insp. Stamp |
|--------------------------------|----------------------------------|----------------------|---------|--------|--------------|---------------|---------------|------------------|----------------|
| Draw Nbr | Revision Nbr | | | | | | | | |
| D4635 | E | | | | | | | | |
| 100 | | 0.00 | | | | | | | |
| *100* | | | | | | | | | |
| HandThermo | Memo | 0.00 | | | | | | | |
| Hand Finishing Thermoforming | Pick Kit | | | | | | | | |
| 110 | | 0.00 | | | | | | | |
| *110* | | | | | | | | | |
| Small Fab | Memo | 0.00 | | | | | | | |
| Small Fab | 1- Assemble as per Dwg D4635-043 | | | | | | | | |
| | 2-Install speaker | | | | | | | | |
| | 3- Install Air valve | | | | | | | | |
| | 4-Install Wiring Harness | | | | | | | | |
| | 5-Install wiring harness | | | | | | | | |

DAS
 27
 9-08
 14/10/19

DAS
 27
 9-09
 14/10/19

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

| | | |
|--|--|---|
| Work Order: _____ Part No. _____ NCR No. _____ | DISPOSITION Rework <input type="checkbox"/> Scrap <input type="checkbox"/> Use-as-is <input type="checkbox"/> Suspected Unapproved <input type="checkbox"/> | AGAINST DEPARTMENT/PROCESS <div style="display: flex; justify-content: space-between;"> <div> Skid-tube <input type="checkbox"/> Machining <input type="checkbox"/> Thermoforming <input type="checkbox"/> Large Fab <input type="checkbox"/> </div> <div> Crosstube <input type="checkbox"/> Small Fab <input type="checkbox"/> Finishing <input type="checkbox"/> Composite <input type="checkbox"/> </div> <div> Water Jet <input type="checkbox"/> Prod. Eng. Coord. <input type="checkbox"/> Rec/Store/Packaging <input type="checkbox"/> Supplier <input type="checkbox"/> </div> <div> Engineering <input type="checkbox"/> Quality <input type="checkbox"/> Other <input type="checkbox"/> </div> </div> |
|--|--|---|

| Root Cause | Date | Step | Qty | Description of work order update or non-conformance | Initial Chief Eng | Action Description | Sign & Date | Verification | QC Inspector |
|---------------|------|------|-----|---|-------------------|--------------------|-------------|--------------|--------------|
| Design | | | | | | | | | |
| Doc/Data | | | | | | | | | |
| Equip/Tooling | | | | | | | | | |
| Handling/Pre | | | | | | | | | |
| Material | | | | | | | | | |
| Operator | | | | | | | | | |
| Offset/Setup | | | | | | | | | |
| Process | | | | | | | | | |
| Supplier | | | | | | | | | |
| Training | | | | | | | | | |
| Transport | | | | | | | | | |
| Unapproved | | | | | | | | | |

FAULT CATEGORY

| | | | |
|--|--|---|--|
| Landing Gear <input type="checkbox"/> Bending <input type="checkbox"/> Centre Not Concentric <input type="checkbox"/> Cracks <input type="checkbox"/> Crimp/Kink/Ripple/Wave <input type="checkbox"/> Cuffs <input type="checkbox"/> Crushing <input type="checkbox"/> Heat Treat <input type="checkbox"/> Inspection Strip in Tube <input type="checkbox"/> Marks/Chatter <input type="checkbox"/> Turning Sequence <input type="checkbox"/> Wave/Twist in Tube | General <input type="checkbox"/> Bend <input type="checkbox"/> BOM/Route <input type="checkbox"/> Broken/Damage/Defect <input type="checkbox"/> Burrs <input type="checkbox"/> Contamination <input type="checkbox"/> Countersink <input type="checkbox"/> Cut Too Short <input type="checkbox"/> Drawing <input type="checkbox"/> Drill Holes <input type="checkbox"/> Finish <input type="checkbox"/> Fit/Function | <input type="checkbox"/> Folio/Program <input type="checkbox"/> Grain <input type="checkbox"/> Hardware <input type="checkbox"/> Inspection Incomplete/Unqualified <input type="checkbox"/> Instructions Incomplete/Unclear <input type="checkbox"/> Misaligned/off center <input type="checkbox"/> Mislabeled <input type="checkbox"/> Misread <input type="checkbox"/> Off-set <input type="checkbox"/> Out of Calibration <input type="checkbox"/> Out of Sequence | <input type="checkbox"/> Outside Dimensions <input type="checkbox"/> Over/Under tolerance <input type="checkbox"/> Part Incorrect <input type="checkbox"/> Part Lost/Missing <input type="checkbox"/> Part Moved <input type="checkbox"/> Positioned Wrong <input type="checkbox"/> Power Loss/Surge <input type="checkbox"/> Pressure/Forced <input type="checkbox"/> Set-up <input type="checkbox"/> Temperature/Cure <input type="checkbox"/> Weld <input type="checkbox"/> Wrong Stock Pulled <input type="checkbox"/> Other |
|--|--|---|--|

Work Order ID 124378

September-11-14 12:03:55 PM

124378

Page 2

Item ID: D4635-043 Accept ***N900040100*** Setup Start ***NS1***
 Revision ID: Stop ***NS2***
 Item Name: Aft Ceiling Panel Assembly, LH
 Start Date: 9/10/14 Start Qty: 1.00 ***1*** Cust Item ID:
 Required Date: 9/10/14 Req'd Qty: 1.00 ***1*** Customer:
 Reference:

Approvals: Process Plan: _____ Date: _____ Tooling: _____ Date: _____ Run Start ***NR1***
 QC: _____ Date: _____ SPC (Y/N): _____ Date: _____ Stop ***NR2***

| Sequence ID/ Work Center ID | Operation Description | Set Up/ Run Hours | Tool ID | Tool # | Plan Code | Accept Qty | Reject Qty | Reject Number | Insp. Stamp |
|--------------------------------|--------------------------|----------------------|---------|--------|--------------|---------------|---------------|------------------|----------------|
|--------------------------------|--------------------------|----------------------|---------|--------|--------------|---------------|---------------|------------------|----------------|

| | | | | | | | | | |
|-----------------|---|------|--|--|--|--|--|--|--|
| 120 | QC5- Inspect part completeness to step on W/O | 0.00 | | | | | | | |
| *120* | | | | | | | | | |
| QC | Memo | 0.00 | | | | | | | |
| Quality Control | | | | | | | | | |

| | | | | | | | | | |
|--------------|---|------|--|--|--|--|--|--|--|
| 130 | Identify as per dwg & Stock Location: _____ | 0.00 | | | | | | | |
| *130* | | | | | | | | | |
| Packaging | Memo | 0.00 | | | | | | | |
| Packaging | | | | | | | | | |

| | | | | | | | | | |
|-----------------|---|------|--|--|--|--|--|--|--|
| 140 | QC21- Final Inspection - Work Order Release | 0.00 | | | | | | | |
| *140* | | | | | | | | | |
| QC | Memo | 0.00 | | | | | | | |
| Quality Control | | | | | | | | | |

PP 12499p

OCT 22 2014

DAS
06
9-62

14/10/22

mf
14-10-22

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

| | | | | | | |
|--|--|--|--|--|---|--|
| Work Order: _____ Part No. _____ NCR No. _____ | DISPOSITION Rework <input type="checkbox"/> Scrap <input type="checkbox"/> Use-as-is <input type="checkbox"/> Suspected Unapproved <input type="checkbox"/> | AGAINST DEPARTMENT/PROCESS <table style="width: 100%;"> <tr> <td style="width: 33%;"> Skid-tube <input type="checkbox"/> Machining <input type="checkbox"/> Thermoforming <input type="checkbox"/> Large Fab <input type="checkbox"/> </td> <td style="width: 33%;"> Crosstube <input type="checkbox"/> Small Fab <input type="checkbox"/> Finishing <input type="checkbox"/> Composite <input type="checkbox"/> </td> <td style="width: 33%;"> Water Jet <input type="checkbox"/> Prod. Eng. Coord. <input type="checkbox"/> Rec/Store/Packaging <input type="checkbox"/> Supplier <input type="checkbox"/> </td> <td style="width: 33%;"> Engineering <input type="checkbox"/> Quality <input type="checkbox"/> Other <input type="checkbox"/> </td> </tr> </table> | Skid-tube <input type="checkbox"/> Machining <input type="checkbox"/> Thermoforming <input type="checkbox"/> Large Fab <input type="checkbox"/> | Crosstube <input type="checkbox"/> Small Fab <input type="checkbox"/> Finishing <input type="checkbox"/> Composite <input type="checkbox"/> | Water Jet <input type="checkbox"/> Prod. Eng. Coord. <input type="checkbox"/> Rec/Store/Packaging <input type="checkbox"/> Supplier <input type="checkbox"/> | Engineering <input type="checkbox"/> Quality <input type="checkbox"/> Other <input type="checkbox"/> |
| Skid-tube <input type="checkbox"/> Machining <input type="checkbox"/> Thermoforming <input type="checkbox"/> Large Fab <input type="checkbox"/> | Crosstube <input type="checkbox"/> Small Fab <input type="checkbox"/> Finishing <input type="checkbox"/> Composite <input type="checkbox"/> | Water Jet <input type="checkbox"/> Prod. Eng. Coord. <input type="checkbox"/> Rec/Store/Packaging <input type="checkbox"/> Supplier <input type="checkbox"/> | Engineering <input type="checkbox"/> Quality <input type="checkbox"/> Other <input type="checkbox"/> | | | |

| Root Cause | Date | Step | Qty | Description of work order update or non-conformance | Initial Chief Eng | Action Description | Sign & Date | Verification | QC Inspector |
|---------------|------|------|-----|---|-------------------|--------------------|-------------|--------------|--------------|
| Design | | | | | | | | | |
| Doc/Data | | | | | | | | | |
| Equip/Tooling | | | | | | | | | |
| Handling/Pre | | | | | | | | | |
| Material | | | | | | | | | |
| Operator | | | | | | | | | |
| Offset/Setup | | | | | | | | | |
| Process | | | | | | | | | |
| Supplier | | | | | | | | | |
| Training | | | | | | | | | |
| Transport | | | | | | | | | |
| Unapproved | | | | | | | | | |

FAULT CATEGORY

| | | | |
|--|--|---|--|
| Landing Gear <input type="checkbox"/> Bending <input type="checkbox"/> Centre Not Concentric <input type="checkbox"/> Cracks <input type="checkbox"/> Crimp/Kink/Ripple/Wave <input type="checkbox"/> Cuffs <input type="checkbox"/> Crushing <input type="checkbox"/> Heat Treat <input type="checkbox"/> Inspection Strip in Tube <input type="checkbox"/> Marks/Chatter <input type="checkbox"/> Turning Sequence <input type="checkbox"/> Wave/Twist in Tube | General <input type="checkbox"/> Bend <input type="checkbox"/> BOM/Route <input type="checkbox"/> Broken/Damage/Defect <input type="checkbox"/> Burrs <input type="checkbox"/> Contamination <input type="checkbox"/> Countersink <input type="checkbox"/> Cut Too Short <input type="checkbox"/> Drawing <input type="checkbox"/> Drill Holes <input type="checkbox"/> Finish <input type="checkbox"/> Fit/Function | <input type="checkbox"/> Folio/Program <input type="checkbox"/> Grain <input type="checkbox"/> Hardware <input type="checkbox"/> Inspection Incomplete/Unqualified <input type="checkbox"/> Instructions Incomplete/Unclear <input type="checkbox"/> Misaligned/off center <input type="checkbox"/> Mislabeled <input type="checkbox"/> Misread <input type="checkbox"/> Off-set <input type="checkbox"/> Out of Calibration <input type="checkbox"/> Out of Sequence | <input type="checkbox"/> Outside Dimensions <input type="checkbox"/> Over/Under tolerance <input type="checkbox"/> Part Incorrect <input type="checkbox"/> Part Lost/Missing <input type="checkbox"/> Part Moved <input type="checkbox"/> Positioned Wrong <input type="checkbox"/> Power Loss/Surge <input type="checkbox"/> Pressure/Forced Set-up <input type="checkbox"/> Temperature/Cure <input type="checkbox"/> Weld <input type="checkbox"/> Wrong Stock Pulled <input type="checkbox"/> Other |
|--|--|---|--|

Picklist Print

September-11-14 12:03:54 PM

Page 1

Work Order ID: 124378

124378

Parent Item: D4635-043

D4635-043

Parent Item Name: Aft Ceiling Panel Assembly, LH

Start Date: 9/10/14

Required Date: 9/10/14

Start Qty: 1.00

Required Qty: 1.00

Comments:

IPP Rev. A 12/08/09 New Issue DL
12/11/08 Doc Release DL
13/07/09 DL verf:DD

IPP Rev B
IPP Rev C Dwg. Update
IPP Rev D Dwg Update 14/01/20 DL

| Component Item ID/ Item Name | Replacement Item ID | Mfg/ Purch | Bin Item | Primary Location | Last Location | Route Seq ID | Unit of Measure | Qty on Hand | Qty per Kit | Total Qty | Qty Issued | Date Issued | Status |
|---------------------------------|------------------------|---------------|-------------|---------------------|------------------|-----------------|--------------------|----------------|-------------|--------------|---------------|----------------|--------|
|---------------------------------|------------------------|---------------|-------------|---------------------|------------------|-----------------|--------------------|----------------|-------------|--------------|---------------|----------------|--------|

MS24693-BB51

Purchased

No

100

Each

731.0000

4

4

**

14/10/14

DAS
27
9-89

MS24693-BB51

Screw

Location

Loc Qty

Loc Code

ST296

731

m128057

731

D4635-143

Manufactured

No

100

Each

2.0000

1

1

**

14/10/14

DAS
27
9-89

D4635-143

Aft Ceiling Replacement Panel Assembly, LH

Location

Loc Qty

Loc Code

MF

2

122736

1

122737

1

D4646-1

Manufactured

No

100

Each

30.0000

1

1

**

14/10/14

DAS
27
9-89

D4646-1

Plenum Cap Assembly

Location

Loc Qty

Loc Code

MF3

30

121007

30

D4652-1

Manufactured

No

100

Each

0.0000

1

1

**

14/10/14

DAS
27
9-89

D4652-1

Air Valve, 1.16 Id Disk Type

B112003

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

| | | | | | | |
|--|--|--|--|--|---|--|
| Work Order: _____ Part No. _____ NCR No. _____ | DISPOSITION Rework <input type="checkbox"/> Scrap <input type="checkbox"/> Use-as-is <input type="checkbox"/> Suspected Unapproved <input type="checkbox"/> | <table style="width:100%;"> <tr> <td style="width:33%;"> Skid-tube <input type="checkbox"/> Machining <input type="checkbox"/> Thermoforming <input type="checkbox"/> Large Fab <input type="checkbox"/> </td> <td style="width:33%;"> Crosstube <input type="checkbox"/> Small Fab <input type="checkbox"/> Finishing <input type="checkbox"/> Composite <input type="checkbox"/> </td> <td style="width:33%;"> Water Jet <input type="checkbox"/> Prod. Eng. Coord. <input type="checkbox"/> Rec/Store/Packaging <input type="checkbox"/> Supplier <input type="checkbox"/> </td> <td style="width:33%;"> Engineering <input type="checkbox"/> Quality <input type="checkbox"/> Other <input type="checkbox"/> </td> </tr> </table> | Skid-tube <input type="checkbox"/> Machining <input type="checkbox"/> Thermoforming <input type="checkbox"/> Large Fab <input type="checkbox"/> | Crosstube <input type="checkbox"/> Small Fab <input type="checkbox"/> Finishing <input type="checkbox"/> Composite <input type="checkbox"/> | Water Jet <input type="checkbox"/> Prod. Eng. Coord. <input type="checkbox"/> Rec/Store/Packaging <input type="checkbox"/> Supplier <input type="checkbox"/> | Engineering <input type="checkbox"/> Quality <input type="checkbox"/> Other <input type="checkbox"/> |
| Skid-tube <input type="checkbox"/> Machining <input type="checkbox"/> Thermoforming <input type="checkbox"/> Large Fab <input type="checkbox"/> | Crosstube <input type="checkbox"/> Small Fab <input type="checkbox"/> Finishing <input type="checkbox"/> Composite <input type="checkbox"/> | Water Jet <input type="checkbox"/> Prod. Eng. Coord. <input type="checkbox"/> Rec/Store/Packaging <input type="checkbox"/> Supplier <input type="checkbox"/> | Engineering <input type="checkbox"/> Quality <input type="checkbox"/> Other <input type="checkbox"/> | | | |

| Root Cause | Date | Step | Qty | Description of work order update or non-conformance | Initial Chief Eng | Action Description | Sign & Date | Verification | QC Inspector |
|---------------|------|------|-----|---|-------------------|--------------------|-------------|--------------|--------------|
| Design | | | | | | | | | |
| Doc/Data | | | | | | | | | |
| Equip/Tooling | | | | | | | | | |
| Handling/Pre | | | | | | | | | |
| Material | | | | | | | | | |
| Operator | | | | | | | | | |
| Offset/Setup | | | | | | | | | |
| Process | | | | | | | | | |
| Supplier | | | | | | | | | |
| Training | | | | | | | | | |
| Transport | | | | | | | | | |
| Unapproved | | | | | | | | | |

FAULT CATEGORY

| | | | |
|--|--|---|--|
| Landing Gear <input type="checkbox"/> Bending <input type="checkbox"/> Centre Not Concentric <input type="checkbox"/> Cracks <input type="checkbox"/> Crimp/Kink/Ripple/Wave <input type="checkbox"/> Cuffs <input type="checkbox"/> Crushing <input type="checkbox"/> Heat Treat <input type="checkbox"/> Inspection Strip in Tube <input type="checkbox"/> Marks/Chatter <input type="checkbox"/> Turning Sequence <input type="checkbox"/> Wave/Twist in Tube | General <input type="checkbox"/> Bend <input type="checkbox"/> BOM/Route <input type="checkbox"/> Broken/Damage/Defect <input type="checkbox"/> Burrs <input type="checkbox"/> Contamination <input type="checkbox"/> Countersink <input type="checkbox"/> Cut Too Short <input type="checkbox"/> Drawing <input type="checkbox"/> Drill Holes <input type="checkbox"/> Finish <input type="checkbox"/> Fit/Function | <input type="checkbox"/> Folio/Program <input type="checkbox"/> Grain <input type="checkbox"/> Hardware <input type="checkbox"/> Inspection Incomplete/Unqualified <input type="checkbox"/> Instructions Incomplete/Unclear <input type="checkbox"/> Misaligned/off center <input type="checkbox"/> Mislabeled <input type="checkbox"/> Misread <input type="checkbox"/> Off-set <input type="checkbox"/> Out of Calibration <input type="checkbox"/> Out of Sequence | <input type="checkbox"/> Outside Dimensions <input type="checkbox"/> Over/Under tolerance <input type="checkbox"/> Part Incorrect <input type="checkbox"/> Part Lost/Missing <input type="checkbox"/> Part Moved <input type="checkbox"/> Positioned Wrong <input type="checkbox"/> Power Loss/Surge <input type="checkbox"/> Pressure/Forced <input type="checkbox"/> Set-up <input type="checkbox"/> Temperature/Cure <input type="checkbox"/> Weld <input type="checkbox"/> Wrong Stock Pulled <input type="checkbox"/> Other |
|--|--|---|--|

Picklist Print

September-11-14 12:03:54 PM

Page 2

Work Order ID: 124378

Parent Item: D4635-043

Parent Item Name: Aft Ceiling Panel Assembly, LH

124378

D4635-043

Start Date: 9/10/14

Required Date: 9/10/14

Start Qty: 1.00

Required Qty: 1.00

D4655-1

Manufactured No

100

Each

147.0000

1

1

D4655-1

Speaker

14/10/19 DAS 27 9:59

Location

Loc Qty

Loc Code

MF

21

117634

21

MF3

63

111827

15

92333

6

93061

42

MF4

14

117634

14

MF5

14

112008

14

ST071

35

112009

35

D4708-9

Manufactured No

100

Each

74.0000

1

1

D4708-9

Lanyard

14/10/19 DAS 27 9:59

Location

Loc Qty

Loc Code

MF3

74

112122

74

D4728-045

Manufactured No

100

Each

14.0000

1

1

D4728-045

LH Cabin Speaker #3

14/10/19 DAS 27 9:59

Location

Loc Qty

Loc Code

MF

14

117927

14

September-11-14 12:03:54 PM

Shop Packet Print

Page 2

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

| | | |
|--|--|---|
| Work Order: _____ Part No. _____ NCR No. _____ | DISPOSITION Rework <input type="checkbox"/> Scrap <input type="checkbox"/> Use-as-is <input type="checkbox"/> Suspected Unapproved <input type="checkbox"/> | AGAINST DEPARTMENT/PROCESS <div style="display: flex; justify-content: space-between;"> <div> Skid-tube <input type="checkbox"/> Machining <input type="checkbox"/> Thermoforming <input type="checkbox"/> Large Fab <input type="checkbox"/> </div> <div> Crosstube <input type="checkbox"/> Small Fab <input type="checkbox"/> Finishing <input type="checkbox"/> Composite <input type="checkbox"/> </div> <div> Water Jet <input type="checkbox"/> Prod. Eng. Coord. <input type="checkbox"/> Rec/Store/Packaging <input type="checkbox"/> Supplier <input type="checkbox"/> </div> <div> Engineering <input type="checkbox"/> Quality <input type="checkbox"/> Other <input type="checkbox"/> </div> </div> |
|--|--|---|

| Root Cause | Date | Step | Qty | Description of work order update or non-conformance | Initial Chief Eng | Action Description | Sign & Date | Verification | QC Inspector |
|---------------|------|------|-----|---|-------------------|--------------------|-------------|--------------|--------------|
| Design | | | | | | | | | |
| Doc/Data | | | | | | | | | |
| Equip/Tooling | | | | | | | | | |
| Handling/Pre | | | | | | | | | |
| Material | | | | | | | | | |
| Operator | | | | | | | | | |
| Offset/Setup | | | | | | | | | |
| Process | | | | | | | | | |
| Supplier | | | | | | | | | |
| Training | | | | | | | | | |
| Transport | | | | | | | | | |
| Unapproved | | | | | | | | | |

FAULT CATEGORY

| | | | |
|--|--|---|--|
| Landing Gear <input type="checkbox"/> Bending <input type="checkbox"/> Centre Not Concentric <input type="checkbox"/> Cracks <input type="checkbox"/> Crimp/Kink/Ripple/Wave <input type="checkbox"/> Cuffs <input type="checkbox"/> Crushing <input type="checkbox"/> Heat Treat <input type="checkbox"/> Inspection Strip in Tube <input type="checkbox"/> Marks/Chatter <input type="checkbox"/> Turning Sequence <input type="checkbox"/> Wave/Twist in Tube | General <input type="checkbox"/> Bend <input type="checkbox"/> BOM/Route <input type="checkbox"/> Broken/Damage/Defect <input type="checkbox"/> Burrs <input type="checkbox"/> Contamination <input type="checkbox"/> Countersink <input type="checkbox"/> Cut Too Short <input type="checkbox"/> Drawing <input type="checkbox"/> Drill Holes <input type="checkbox"/> Finish <input type="checkbox"/> Fit/Function | <input type="checkbox"/> Folio/Program <input type="checkbox"/> Grain <input type="checkbox"/> Hardware <input type="checkbox"/> Inspection Incomplete/Unqualified <input type="checkbox"/> Instructions Incomplete/Unclear <input type="checkbox"/> Misaligned/off center <input type="checkbox"/> Mislabeled <input type="checkbox"/> Misread <input type="checkbox"/> Off-set <input type="checkbox"/> Out of Calibration <input type="checkbox"/> Out of Sequence | <input type="checkbox"/> Outside Dimensions <input type="checkbox"/> Over/Under tolerance <input type="checkbox"/> Part Incorrect <input type="checkbox"/> Part Lost/Missing <input type="checkbox"/> Part Moved <input type="checkbox"/> Positioned Wrong <input type="checkbox"/> Power Loss/Surge <input type="checkbox"/> Pressure/Forced <input type="checkbox"/> Set-up <input type="checkbox"/> Temperature/Cure <input type="checkbox"/> Weld <input type="checkbox"/> Wrong Stock Pulled <input type="checkbox"/> Other |
|--|--|---|--|

Picklist Print

September-11-14 12:03:54 PM

Page 3

Work Order ID: 124378

124378

Parent Item: D4635-043

D4635-043

Parent Item Name: Aft Ceiling Panel Assembly, LH

Start Date: 9/10/14

Required Date: 9/10/14

Start Qty: 1.00

Required Qty: 1.00

D4728-061

Manufactured No

100 Each

14.0000

1

1

D4728-061

Cabin Lights Control Relay

14/10/14

DAS
27
9-59

Location

Loc Qty

Loc Code

MF

14

117937

14

D4743-1

Manufactured No

100 Each

29.0000

1

1

D4743-1

Speaker Grill

14/10/14

DAS
27
9-59

Location

Loc Qty

Loc Code

MF

29

122488

29

MS21044-N08

Purchased No

100 Each

289.0000

4

4

MS21044-N08

Nut

14/10/14

DAS
27
9-59

Location

Loc Qty

Loc Code

ST306

289

123741

7

m127813

10

m128300

1

m128429

13

m128578

6

m128650

14

m129499

28

m129630

10

m130297

200

4

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

| | | | | | | | | | | | | | | | | | | |
|--|--|--|--------------------------------------|------------------------------------|------------------------------------|--------------------------------------|------------------------------------|------------------------------------|--|----------------------------------|--|------------------------------------|--|--------------------------------|------------------------------------|------------------------------------|-----------------------------------|--|
| Work Order: _____ Part No. _____ NCR No. _____ | DISPOSITION Rework <input type="checkbox"/> Scrap <input type="checkbox"/> Use-as-is <input type="checkbox"/> Suspected Unapproved <input type="checkbox"/> | AGAINST DEPARTMENT/PROCESS <table style="width:100%;"> <tr> <td>Skid-tube <input type="checkbox"/></td> <td>Crosstube <input type="checkbox"/></td> <td>Water Jet <input type="checkbox"/></td> <td>Engineering <input type="checkbox"/></td> </tr> <tr> <td>Machining <input type="checkbox"/></td> <td>Small Fab <input type="checkbox"/></td> <td>Prod. Eng. Coord. <input type="checkbox"/></td> <td>Quality <input type="checkbox"/></td> </tr> <tr> <td>Thermoforming <input type="checkbox"/></td> <td>Finishing <input type="checkbox"/></td> <td>Rec/Store/Packaging <input type="checkbox"/></td> <td>Other <input type="checkbox"/></td> </tr> <tr> <td>Large Fab <input type="checkbox"/></td> <td>Composite <input type="checkbox"/></td> <td>Supplier <input type="checkbox"/></td> <td></td> </tr> </table> | Skid-tube <input type="checkbox"/> | Crosstube <input type="checkbox"/> | Water Jet <input type="checkbox"/> | Engineering <input type="checkbox"/> | Machining <input type="checkbox"/> | Small Fab <input type="checkbox"/> | Prod. Eng. Coord. <input type="checkbox"/> | Quality <input type="checkbox"/> | Thermoforming <input type="checkbox"/> | Finishing <input type="checkbox"/> | Rec/Store/Packaging <input type="checkbox"/> | Other <input type="checkbox"/> | Large Fab <input type="checkbox"/> | Composite <input type="checkbox"/> | Supplier <input type="checkbox"/> | |
| Skid-tube <input type="checkbox"/> | Crosstube <input type="checkbox"/> | Water Jet <input type="checkbox"/> | Engineering <input type="checkbox"/> | | | | | | | | | | | | | | | |
| Machining <input type="checkbox"/> | Small Fab <input type="checkbox"/> | Prod. Eng. Coord. <input type="checkbox"/> | Quality <input type="checkbox"/> | | | | | | | | | | | | | | | |
| Thermoforming <input type="checkbox"/> | Finishing <input type="checkbox"/> | Rec/Store/Packaging <input type="checkbox"/> | Other <input type="checkbox"/> | | | | | | | | | | | | | | | |
| Large Fab <input type="checkbox"/> | Composite <input type="checkbox"/> | Supplier <input type="checkbox"/> | | | | | | | | | | | | | | | | |

| Root Cause | Date | Step | Qty | Description of work order update or non-conformance | Initial Chief Eng | Action Description | Sign & Date | Verification | QC Inspector |
|---------------|------|------|-----|---|-------------------|--------------------|-------------|--------------|--------------|
| Design | | | | | | | | | |
| Doc/Data | | | | | | | | | |
| Equip/Tooling | | | | | | | | | |
| Handling/Pre | | | | | | | | | |
| Material | | | | | | | | | |
| Operator | | | | | | | | | |
| Offset/Setup | | | | | | | | | |
| Process | | | | | | | | | |
| Supplier | | | | | | | | | |
| Training | | | | | | | | | |
| Transport | | | | | | | | | |
| Unapproved | | | | | | | | | |

FAULT CATEGORY

| | | | |
|--|--|---|--|
| Landing Gear <input type="checkbox"/> Bending <input type="checkbox"/> Centre Not Concentric <input type="checkbox"/> Cracks <input type="checkbox"/> Crimp/Kink/Ripple/Wave <input type="checkbox"/> Cuffs <input type="checkbox"/> Crushing <input type="checkbox"/> Heat Treat <input type="checkbox"/> Inspection Strip in Tube <input type="checkbox"/> Marks/Chatter <input type="checkbox"/> Turning Sequence <input type="checkbox"/> Wave/Twist in Tube | General <input type="checkbox"/> Bend <input type="checkbox"/> BOM/Route <input type="checkbox"/> Broken/Damage/Defect <input type="checkbox"/> Burrs <input type="checkbox"/> Contamination <input type="checkbox"/> Countersink <input type="checkbox"/> Cut Too Short <input type="checkbox"/> Drawing <input type="checkbox"/> Drill Holes <input type="checkbox"/> Finish <input type="checkbox"/> Fit/Function | <input type="checkbox"/> Folio/Program <input type="checkbox"/> Grain <input type="checkbox"/> Hardware <input type="checkbox"/> Inspection Incomplete/Unqualified <input type="checkbox"/> Instructions Incomplete/Unclear <input type="checkbox"/> Misaligned/off center <input type="checkbox"/> Mislabeled <input type="checkbox"/> Misread <input type="checkbox"/> Off-set <input type="checkbox"/> Out of Calibration <input type="checkbox"/> Out of Sequence | <input type="checkbox"/> Outside Dimensions <input type="checkbox"/> Over/Under tolerance <input type="checkbox"/> Part Incorrect <input type="checkbox"/> Part Lost/Missing <input type="checkbox"/> Part Moved <input type="checkbox"/> Positioned Wrong <input type="checkbox"/> Power Loss/Surge <input type="checkbox"/> Pressure/Forced <input type="checkbox"/> Set-up <input type="checkbox"/> Temperature/Cure <input type="checkbox"/> Weld <input type="checkbox"/> Wrong Stock Pulled <input type="checkbox"/> Other |
|--|--|---|--|

Picklist Print

September-11-14 12:03:54 PM

Page 4

Work Order ID: 124378

Parent Item: D4635-043

Parent Item Name: Aft Ceiling Panel Assembly, LH

124378

D4635-043

Start Date: 9/10/14

Required Date: 9/10/14

Start Qty: 1.00

Required Qty: 1.00

MS21919-WDG8

Purchased

No

100

Each

275.0000

3

3

MS21919-WDG8

Clamp

DAS
27
9-10
14/10/14

Location

Loc Qty

Loc Code

MF4

275

123900

4

m128057

271

NAS1149DN832J

Purchased

No

100

Each

2,109.000

4

4

NAS1149DN832J

Washer

DAS
27
9-10
14/10/14

Location

Loc Qty

Loc Code

ST277

2109

M128948

147

124555

145

M126319

11

M127255

160

M128429

883

M129499

463

M129541

300

PLT1.5M-M

Purchased

No

100

Each

1,076.000

3

3

PI T1 5M-M

Tie Wrap

DAS
27
9-10
14/10/14

Location

Loc Qty

Loc Code

MF

74

m126551

74

ST389

1002

124363

2

m129712

1000

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____


Work Order update only ☐

| | | |
|--|--|---|
| Work Order: _____ Part No. _____ NCR No. _____ | DISPOSITION Rework <input type="checkbox"/> Scrap <input type="checkbox"/> Use-as-is <input type="checkbox"/> Suspected Unapproved <input type="checkbox"/> | AGAINST DEPARTMENT/PROCESS <div style="display: flex; justify-content: space-between;"> <div> Skid-tube <input type="checkbox"/> Machining <input type="checkbox"/> Thermoforming <input type="checkbox"/> Large Fab <input type="checkbox"/> </div> <div> Crosstube <input type="checkbox"/> Small Fab <input type="checkbox"/> Finishing <input type="checkbox"/> Composite <input type="checkbox"/> </div> <div> Water Jet <input type="checkbox"/> Prod. Eng. Coord. <input type="checkbox"/> Rec/Store/Packaging <input type="checkbox"/> Supplier <input type="checkbox"/> </div> <div> Engineering <input type="checkbox"/> Quality <input type="checkbox"/> Other <input type="checkbox"/> </div> </div> |
|--|--|---|

| Root Cause | Date | Step | Qty | Description of work order update or non-conformance | Initial Chief Eng | Action Description | Sign & Date | Verification | QC Inspector |
|---------------|------|------|-----|---|-------------------|--------------------|-------------|--------------|--------------|
| Design | | | | | | | | | |
| Doc/Data | | | | | | | | | |
| Equip/Tooling | | | | | | | | | |
| Handling/Pre | | | | | | | | | |
| Material | | | | | | | | | |
| Operator | | | | | | | | | |
| Offset/Setup | | | | | | | | | |
| Process | | | | | | | | | |
| Supplier | | | | | | | | | |
| Training | | | | | | | | | |
| Transport | | | | | | | | | |
| Unapproved | | | | | | | | | |

FAULT CATEGORY

| | | | |
|--|--|---|--|
| Landing Gear <input type="checkbox"/> Bending <input type="checkbox"/> Centre Not Concentric <input type="checkbox"/> Cracks <input type="checkbox"/> Crimp/Kink/Ripple/Wave <input type="checkbox"/> Cuffs <input type="checkbox"/> Crushing <input type="checkbox"/> Heat Treat <input type="checkbox"/> Inspection Strip in Tube <input type="checkbox"/> Marks/Chatter <input type="checkbox"/> Turning Sequence <input type="checkbox"/> Wave/Twist in Tube | General <input type="checkbox"/> Bend <input type="checkbox"/> BOM/Route <input type="checkbox"/> Broken/Damage/Defect <input type="checkbox"/> Burrs <input type="checkbox"/> Contamination <input type="checkbox"/> Countersink <input type="checkbox"/> Cut Too Short <input type="checkbox"/> Drawing <input type="checkbox"/> Drill Holes <input type="checkbox"/> Finish <input type="checkbox"/> Fit/Function | <input type="checkbox"/> Folio/Program <input type="checkbox"/> Grain <input type="checkbox"/> Hardware <input type="checkbox"/> Inspection Incomplete/Unqualified <input type="checkbox"/> Instructions Incomplete/Unclear <input type="checkbox"/> Misaligned/off center <input type="checkbox"/> Mislabeled <input type="checkbox"/> Misread <input type="checkbox"/> Off-set <input type="checkbox"/> Out of Calibration <input type="checkbox"/> Out of Sequence | <input type="checkbox"/> Outside Dimensions <input type="checkbox"/> Over/Under tolerance <input type="checkbox"/> Part Incorrect <input type="checkbox"/> Part Lost/Missing <input type="checkbox"/> Part Moved <input type="checkbox"/> Positioned Wrong <input type="checkbox"/> Power Loss/Surge <input type="checkbox"/> Pressure/Forced <input type="checkbox"/> Set-up <input type="checkbox"/> Temperature/Cure <input type="checkbox"/> Weld <input type="checkbox"/> Wrong Stock Pulled <input type="checkbox"/> Other |
|--|--|---|--|

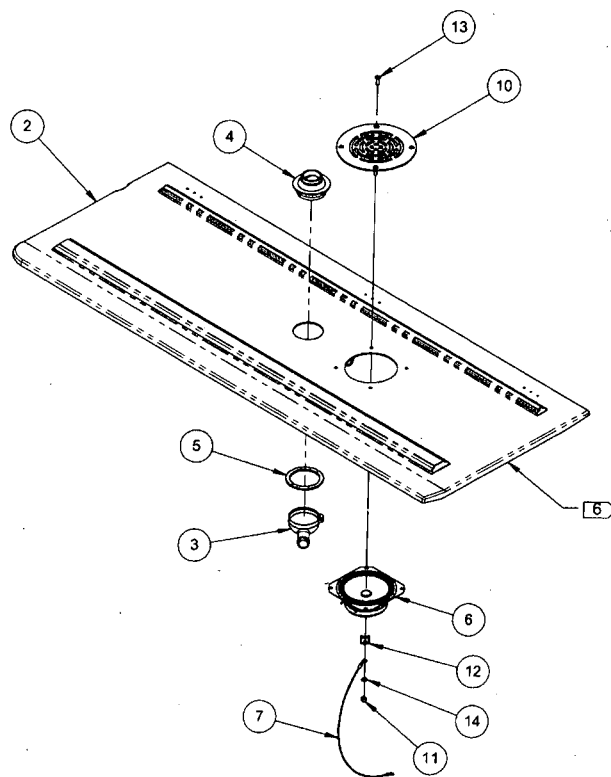

| ITEM NO. | QTY. -043 | PART NUMBER | DESCRIPTION |
|----------|--------------|---------------|---|
| 1 | X | D4635-043 | LH, AFT CEILING PANEL ASSY |
| 2 | 1 | D4635-143 | LH, AFT CEILING REPLACEMENT PANEL ASSY |
| 3 | 1 | D4646-1 | PLENUM CAP ASSEMBLY |
| 4 | 1 | D4652-1 | AIR VALVE |
| 5 | 1 | D4652-3 (REF) | MOUNTING NUT (PART OF D4652-1) |
| 6 | 1 | D4655-1 | SPEAKER |
| 7 | 1 | D4708-9 | LANYARD |
| 8 | 1 | D4728-045 | LH SPEAKER #3 HARNESS ASSEMBLY |
| 9 | 1 | D4728-061 | CABIN LIGHTS CONTROL RELAY HARNESS ASSEMBLY |
| 10 | 1 | D4743-1 | SPEAKER GRILL |
| 11 | 4 | MS21044-N08 | NUT |
| 12 | 3 | MS21919WDG8 | CLAMP |
| 13 | 4 | MS24693-BB51 | SCREW |
| 14 | 4 | NAS1149DN832J | WASHER |
| 15 | 3 | PLT1.5M-M | TIE-WRAP (OR PLT1.5M-C) |

SHOP COPY
RETURN TO
ENGINEERING
UNCONTROLLED COPY
SUBJECT TO AMENDMENT
WITHOUT NOTICE
WORK ORDER
NO. 124378 MJS
14-09-17



RELEASED
2014-01-22

D4635-043 LH, AFT CEILING PANEL ASSY

NOTES:

- 1) MATERIAL: N/A
- 2) FINISH: N/A
- 3) TOLERANCES: PER DART QSI 018 UNLESS OTHERWISE NOTED
- 4) UNITS: INCHES UNLESS OTHERWISE NOTED
- 5) BREAK SHARP EDGES: 0.005 TO 0.010 MAX
- 6) IDENTIFICATION: IDENTIFY PER QSI 044 6.4, ON SMOOTH SIDE
- 7) WEIGHT: 5.0 lbs
- 8) INSTALL D4728-045/-061 WIRE HARNESS PER QSI 048
- 9) ON D4708-9 LANYARD OPEN TO Ø0.196 BOTH ENDS

| | | | |
|------------|----------|---|---------------|
| DESIGN | RF | DART AEROSPACE LTD HAWKESBURY, ONTARIO, CANADA | |
| DRAWN | RF | | |
| CHECKED | DC | DRAWING NO. | REV. E |
| MFG. APPR. | HL | D4635 | SHEET 5 OF 18 |
| APPROVED | HL | TITLE | SCALE |
| DE APPR. | HL | OUTBOARD CEILING PANELS | NTS |
| DATE | 14.01.09 | COPYRIGHT © 2012 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL, AND IS SUPPLIED ON THE EXPRESS UNDERSTANDING THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD. | |

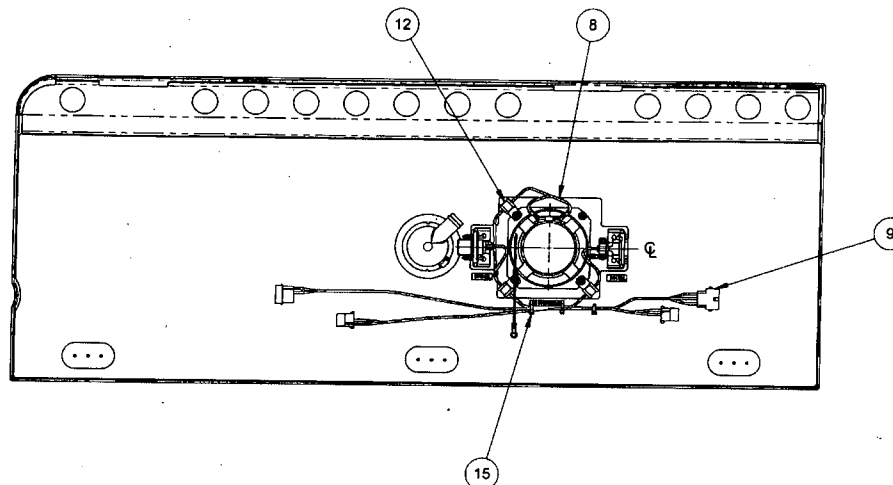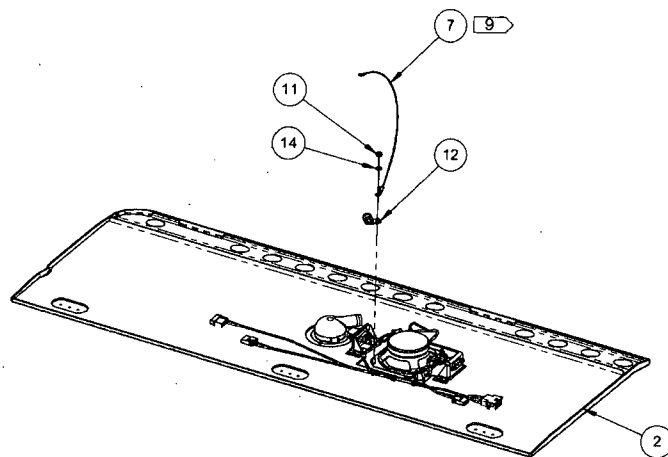

D4635-043 LH, AFT CEILING PANEL ASSY
AUXILIARY VIEW

RELEASED
2014-01-22

| | | | |
|------------|----------|--|--------|
| DESIGN | RF | DART AEROSPACE LTD HAWKESBURY, ONTARIO, CANADA | |
| DRAWN | RF | | |
| CHECKED | DC | DRAWING NO. D4635 | REV. E |
| MFG. APPR. | AK | TITLE | SCALE |
| APPROVED | AK | OUTBOARD CEILING PANELS | |
| DE APPR. | AK | NTS | |
| DATE | 14.01.09 | <small>COPYRIGHT © 2012 BY DART AEROSPACE LTD. THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL, AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.</small> | |
